

# Construction Staging



Jonathan Carver Parkway/11  
**IMPROVEMENTS**

## All Stages of Construction

**APRIL - NOV 2021**

This area of the roadway will be under construction throughout all stages. During this time, the roadway will be shifted to accommodate for two-way traffic.

## Stage 1

**APRIL - JUNE (or last day of school)**

Road will be closed to thru and truck traffic. Local traffic will be maintained to residences and businesses.

## Stage 2\* I I I I I

**JUNE - END OF AUG**

The section of roadway between Ironwood Drive and Dahlgren Road will be fully closed after school has ended.\*

## Stage 2a\*


**8 WEEK PERIOD**

The Dahlgren Road intersection will be closed for roundabout construction.\*

## Stage 3

**SEPT - OCT**

There will be no road closures, and two-way traffic will be maintained while construction is finished.

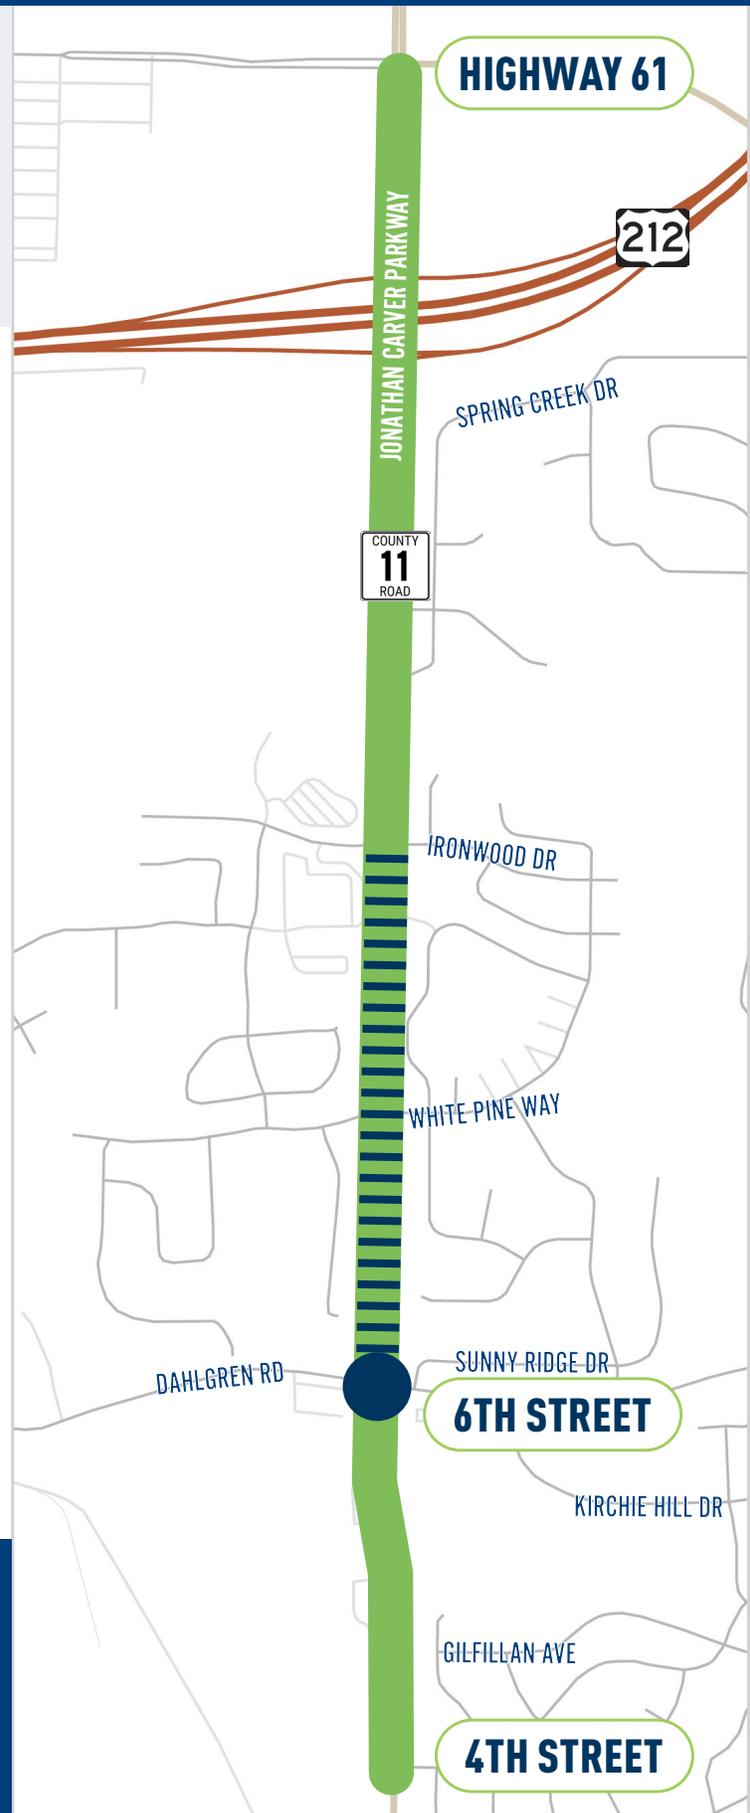

## Project Contact

**Nicole Schmidt**

**612-790-1721**

**carverstreets@bolton-menk.com**
